

FAIRMONT HOMES, INC.

502 S. OAKLAND AVE.
NAPPANEE, IN 46550

Plant Number _____

Date of Manufacture _____	HUD No. _____
---------------------------	---------------

Manufacturer's Serial Number and Model Unit Designation _____

Design Approval by (D.A.P.I.A.) _____

This manufactured home is designed to comply with the Federal Manufactured Home Construction and Safety Standards in force at time of manufacture.
(For additional information, consult owner's manual.)


The factory installed equipment includes:

Equipment	Manufacturer	Model Designation
For heating	_____	_____
Furnace Stack	_____	_____
For Air Cooling	_____	_____
For cooking	_____	_____
Refrigerator	_____	_____
Water Heater	_____	_____
Water Heater Stack	_____	_____
Washer	_____	_____
Clothes Dryer	_____	_____
Dishwasher	_____	_____
Garbage Disposal	_____	_____
Fireplace	_____	_____
Breaker Box	_____	_____
Fan	_____	_____
Microwave	_____	_____
Surface Burner	_____	_____

HOME CONSTRUCTED FOR: Zone I Zone II Zone III


This home has not been designed for the higher wind pressure and anchoring provisions required for ocean/coastal areas and should not be located within 1500' of the coastline in Wind Zones II and III, unless the home and its anchoring and foundation system have been designed for the increased requirements specified for Exposure D in ANSI/ASCE 7-88.

This home has _____ has not _____ been equipped with storm shutters or other protective coverings for windows and exterior door openings. For homes designed to be located in Wind Zones II and III, which have not been provided with shutters or equivalent covering devices, it is strongly recommended that the home be made ready to be equipped with these devices in accordance with the method recommended in manufacturers printed instructions.

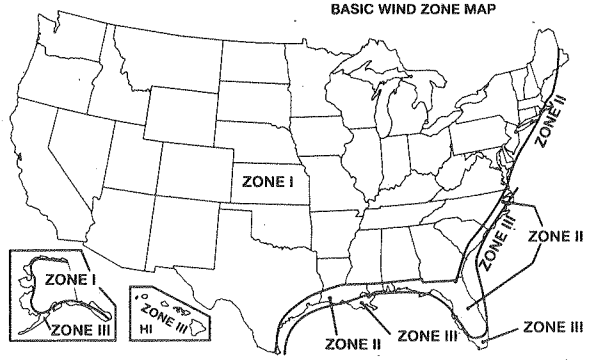

DESIGN ROOF LOAD ZONE MAP

North 40 PSF South 20 PSF
Middle 30 PSF Other _____ PSF

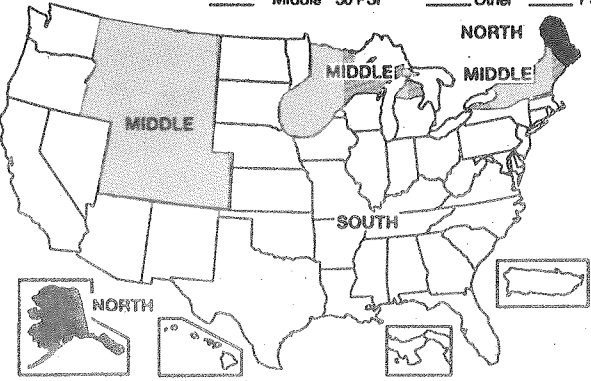

HEATING CERTIFICATE COMFORT HEATING

This manufactured home has been thermally insulated to conform with the requirements of the Federal Manufactured Home Construction and Safety Standards for all locations.
within U/o value zone _____ (See map at bottom)
Heating equipment manufacturer and model (see list at left).
The above heating equipment has the capacity to maintain an average 70° F temperature in this home at outdoor temperature of _____°F.
To maximize furnace operating economy, and to conserve energy, it is recommended that this home be installed where the outdoor winter design temperature (97 1/2%) is not higher than _____ degrees Fahrenheit.

The above information has been calculated assuming a maximum wind velocity of 15 mph at standard atmospheric pressure.

COMFORT COOLING CERTIFICATE

Air conditioner provided at factory (Alternate I)

Air conditioner manufacturer and model (see list at left).
Certified capacity _____ B.T.U./Hour in accordance with the appropriate Air Conditioning and Refrigeration Institute Standards.
This central air conditioning system provided in this home has been sized assuring an orientation of the front (hitch end) of the home facing _____. On this basis the system is designed to maintain an indoor temperature of 75° F when outdoor temperatures are _____°F dry bulb and _____°F wet bulb.

The temperature to which this home can be cooled will change depending upon the amount of exposure of the windows of this home to the sun's radiant heat. Therefore, the home's heat gains will vary dependent upon its orientation to the sun and any permanent shading provided. Information concerning the calculation of cooling loads at various locations, window exposure and shadings are provided in Chapter 22 of the 1989 edition of the ASHRAE Handbook of Fundamentals.

Air conditioner not provided at factory (Alternate II)

The air distribution system of this home is suitable for the installation of central air conditioning. The supply air distribution system installed in this home is sized for a manufactured home central air conditioning system of up to _____ B.T.U./Hr. rated capacity which are certified in accordance with the appropriate Air Conditioning and Refrigeration Institute Standards, when the air circulators of such air conditioners are rated at 0.3 inch water column static pressure or greater for the cooling air delivered to the manufactured home supply air duct system. Information necessary to calculate cooling loads at various locations and orientations is provided in the special comfort cooling information with this manufactured home.

Air conditioning not recommended (Alternate III)

The air distribution system of this home has not been designed in anticipation of its use with a central air conditioning system.

COMFORT COOLING INFORMATION

To determine the required capacity of equipment to cool a home efficiently and economically, a cooling load (heat gain) calculation is required. The cooling load is dependent on the orientation, location and the structure of the home. Central air conditioners operate most efficiently and provide the greatest comfort when their capacity closely approximates the calculated cooling load. Each home's air conditioner should be sized in accordance with Chapter 22 of the American Society of Heating, Refrigerating and Air Conditioning Engineers (ASHRAE) Handbook of Fundamentals 1989 edition, once the location and orientation are known.

INFORMATION PROVIDED BY THE MANUFACTURER NECESSARY TO CALCULATE SENSIBLE HEAT GAIN

- Walls (without windows and doors) "U" _____
- Ceilings Mono "U" _____
- Ceilings Cathedral "U" _____
- Floors "U" _____
- Air ducts in floor "U" _____
- Air ducts in ceiling "U" _____
- Air ducts installed outside the home "U" _____
- Expando ceiling "U" _____
- Expando floor "U" _____

The following are the duct areas in this home:

- Air ducts in floor sq. ft.
- Air ducts in ceiling sq. ft.
- Air ducts outside the home sq. ft.

U/o VALUE ZONE MAP

